

Executive Steering Committee (ESC) Update

Minnesota Eligibility Technology System (METS)

November 15, 2016

Greg Poehling –Director, Program Management Division, MNIT Services @ DHS

- Fall Release Update
- Upcoming Releases – Winter 2016 & 2017
- Brief Updates on Other Roadmaps
- Detailed Project Status Update

Fall Release Update

- Cúram Eligibility System Upgrade deployed weekend of 10/21.
- Production support in place to identify and work defects.
- PMT has prioritized a number of defect fixes which will be part of the Winter Release.
- System is functioning well.

Upcoming Releases


WINTER 2016 RELEASE AND FUTURE RELEASES

- Scope for Winter Release was re-evaluated by PMT and is now slated to include the following:
 - Unique Person ID
 - Defect Fixes from Cúram Upgrade
 - METS-MMIS Interface Improvements


- Some Projects have been Placed on Hold
 - Winter Work
 - MCRE Realignment

Work Incomplete
Work Completed
Work Currently Underway
Work on Hold
XL = "Mega Project"

2016 Release Roadmap

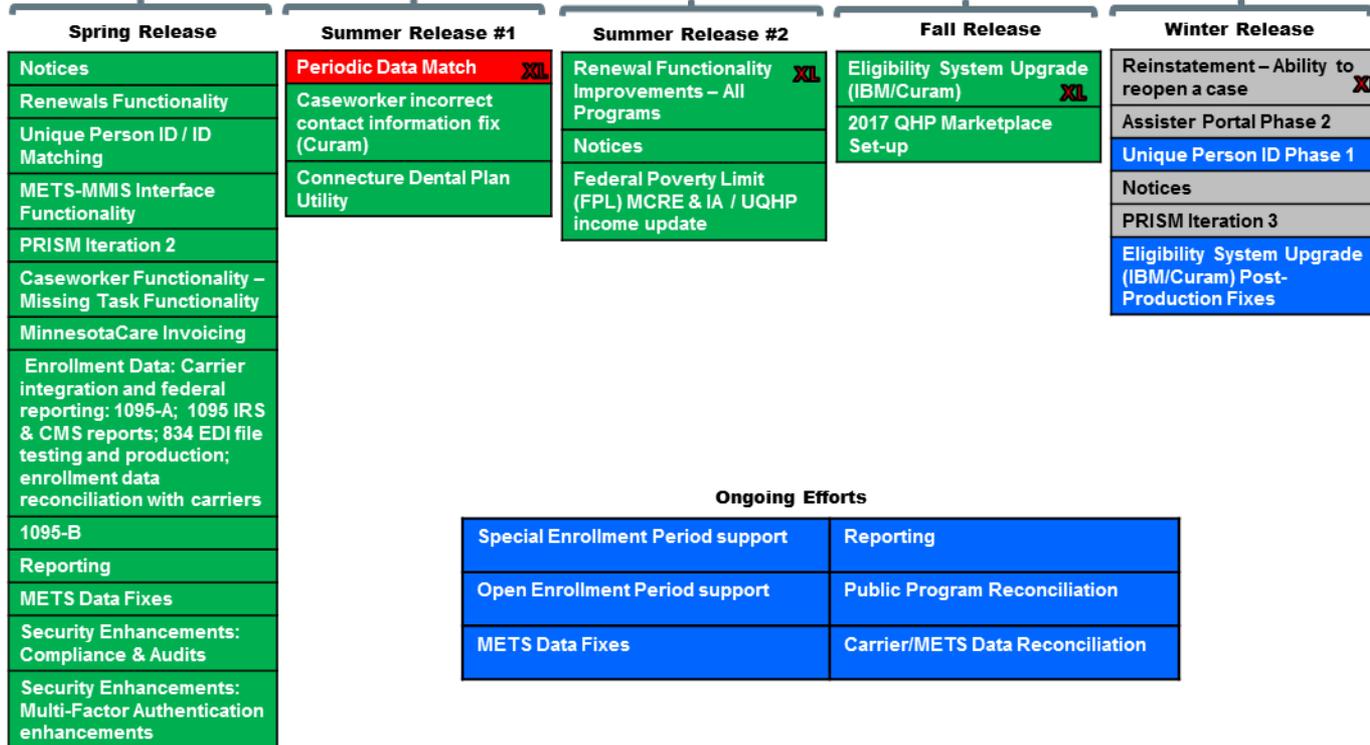


2016 METS Release Deployment Schedule

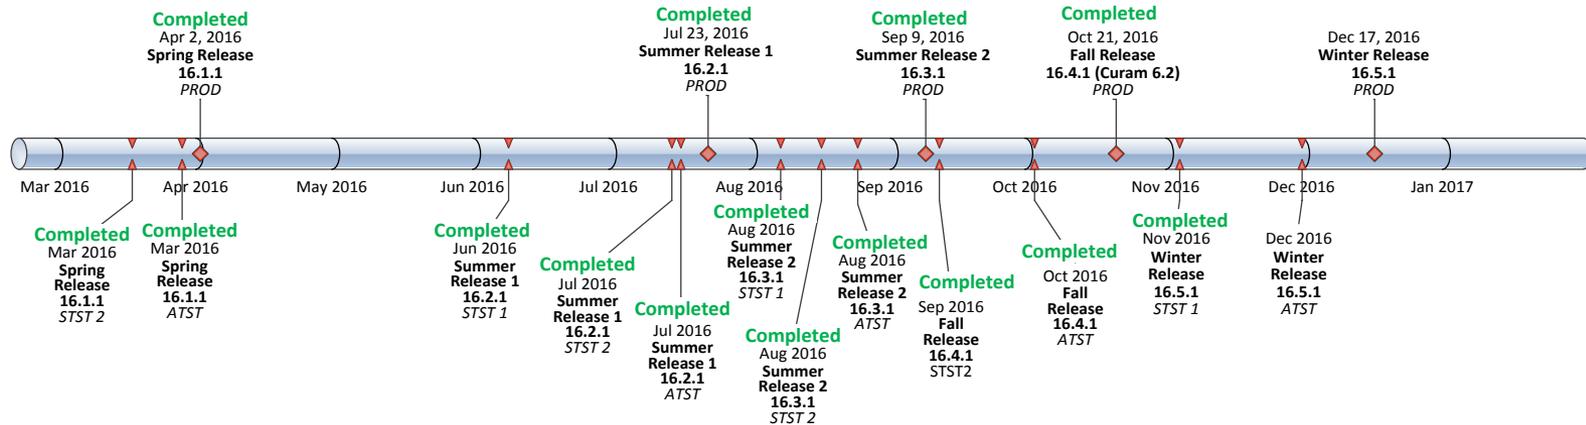

- **STST** – System testing environment. The first step in testing code and projects to ensure functionality is as expected at the technical level.
- **STST2** – Second system testing environment which allows for more code and projects to be tested at the same time.
- **ATST** – User acceptance testing. Final step in testing code and projects before release to ensure functionality is as expected at a user experience level.
- **PROD** – Deploy to production.



2016 IT Release Plan: 1095 Project Roadmap

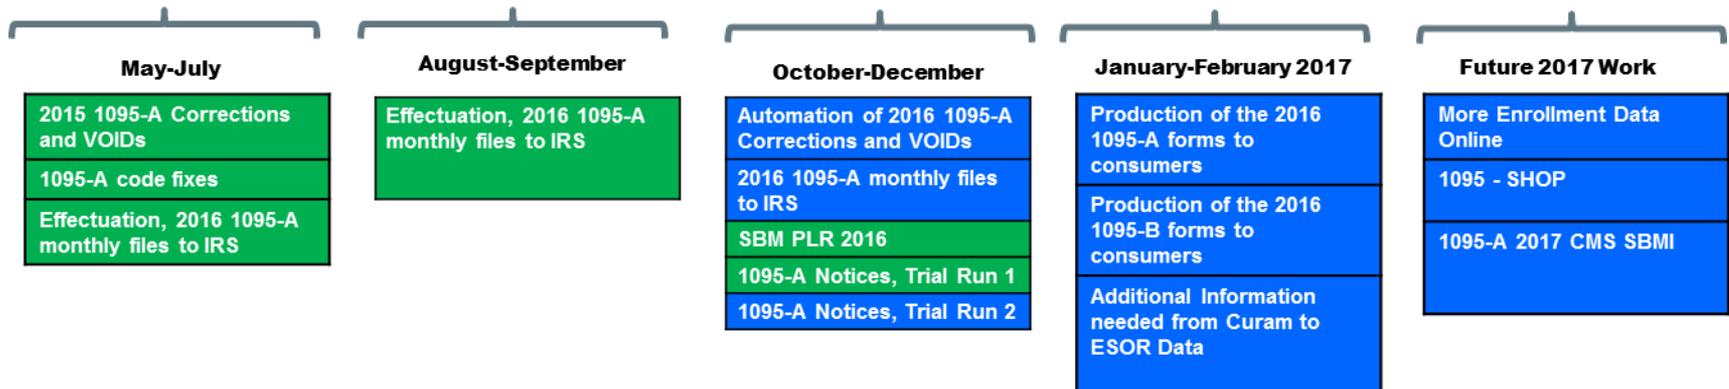

2016 IT Release Plan: ESOR Project Roadmap

Work Incomplete
Work Completed
Work Currently Underway
← = Change in timing
XL = "Mega Project"

August-September

ID Standardization
Passive Renewals

October-December


Coverage System of Record improvements
Passive Renewals
834 Electronic Data Interchange (EDI) Fixes
Automate delivery of EDI files to Carriers
Business Transaction Report (BTR)
Improved Scheduling within ESOR
ESOR Graphical User Improvements

Future 2017 Work

SEP GUI	↔
ESOR Graphical User Interface V. 3	↔

Work Incomplete
Work Completed
Work Currently Underway
Work Waiting Approval
XL = "Mega Project"

2016 IT Release Plan: Other Project Roadmap

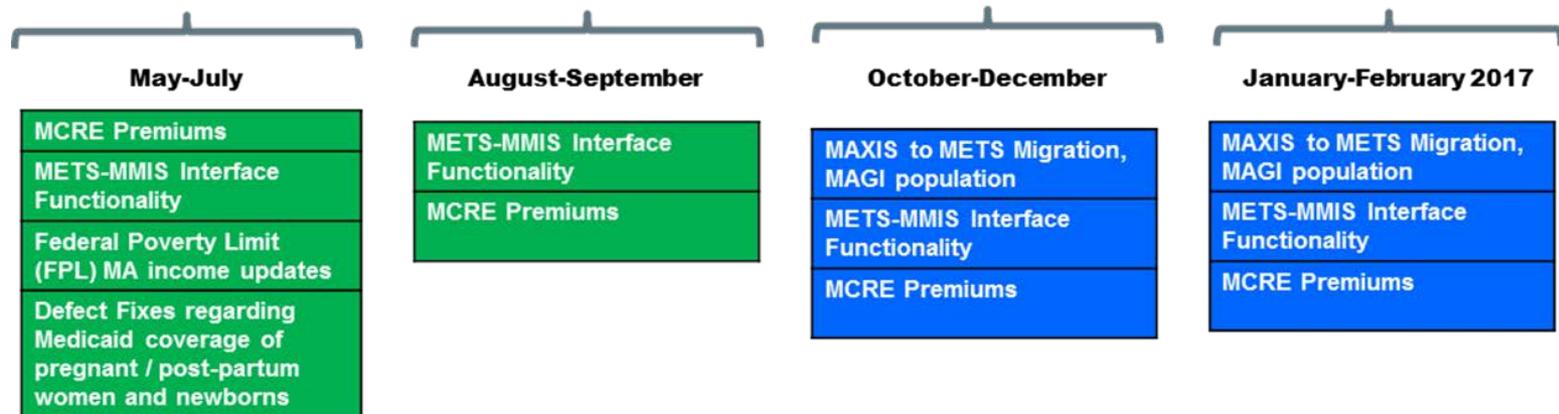

Upcoming Releases

2017 RELEASE PLANNING

PMT Retreat scheduled for 11/17 to plan for 2017– with a focus on the following:

- Identifying and categorizing the work in front of METS PMT
- Outlining strategies and tools for overseeing releases
- Identifying and prioritizing work for 2017

Program Status

As of 11/9/2016

Project Name	Release	Scope	Schedule	Issue	Risk	Overall
1095 Projects	Off Cycle/Non Dev	Green	Green	Green	Yellow	Green
1095-B Phase 2	Off Cycle/Non Dev	Green	Green	Green	Yellow	Green
2017 Marketplace Set-up	Off Cycle/Non Dev	Green	Green	Green	Green	Green
Carrier Reconciliation	Off Cycle/Non Dev	Red	Red	Red	Yellow	Red
Compliance/Audits	Off Cycle/Non Dev	Green	Green	Yellow	Yellow	Yellow
Data Access & Management (Reports)	Off Cycle/Non Dev	Green	Green	Green	Green	Green
ESOR Project	Off Cycle/Non Dev	Green	Red	Yellow	Yellow	Red
Infrastructure Improvements	Off Cycle/Non Dev	Green	Green	Green	Green	Green
MAXIS to METS Migration	Off Cycle/Non Dev	Green	Green	Yellow	Yellow	Yellow
MCRE Premiums - Premium Reconciliation	Off Cycle/Non Dev	Green	Green	Green	Green	Green
MCRE Premiums Phase 3	Off Cycle/Non Dev	Green	Green	Green	Green	Green
METS/MMIS Interface	Off Cycle/Non Dev	Green	Yellow	Yellow	Green	Yellow
METS/Curam Data Work	Off Cycle/Non Dev	Green	Green	Green	Green	Green
METS/Mnsure Connvertex M&O	Off Cycle/Non Dev	Green	Green	Green	Green	Green
Program Reconciliation	Off Cycle/Non Dev	Green	Green	Green	Green	Green
UE/UI Online Application	Off Cycle/Non Dev	Green	Green	Green	Green	Green
Unique Person ID	16.5.1 Winter 2016	Green	Green	Green	Green	Green
Passive Renewals - Project On Hold	Off Cycle/Non Dev	Gray	Gray	Gray	Gray	Gray
Assister Portal Phase 2 - Project On Hold	16.5.1 Winter 2016	Gray	Gray	Gray	Gray	Gray
Notices - Project On Hold	16.5.1 Winter 2016	Gray	Gray	Gray	Gray	Gray
PRISM Iteration 3 - Project On Hold	16.5.1 Winter 2016	Gray	Gray	Gray	Gray	Gray
Reinstatement - Project On Hold	16.5.1 Winter 2016	Gray	Gray	Gray	Gray	Gray
MCRE Realignment (Staggered Renewals) - Project On Hold	17.1.1 Spring 2017	Gray	Gray	Gray	Gray	Gray
